

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Corporate Mental Wellness and Counselling Platform

Name: Aamer Khan SRN: PES1UG24AM902 Section: B Date: 04 October 2026

1. Epics and User Stories (Backlog)

The Lab 1 requirements were grouped into three Epics: Anonymous Identity and Privacy (SCRUM-5), Counselling Booking and Availability (SCRUM-6), and Wellness Assessment and Crisis Support (SCRUM-11). These Epics contain six relevant User Stories worth 31 story points in total. Five stories are High priority and one is Medium priority, keeping privacy, assessment, crisis response, therapist availability and confidential booking ahead of the wellness-trend feature.

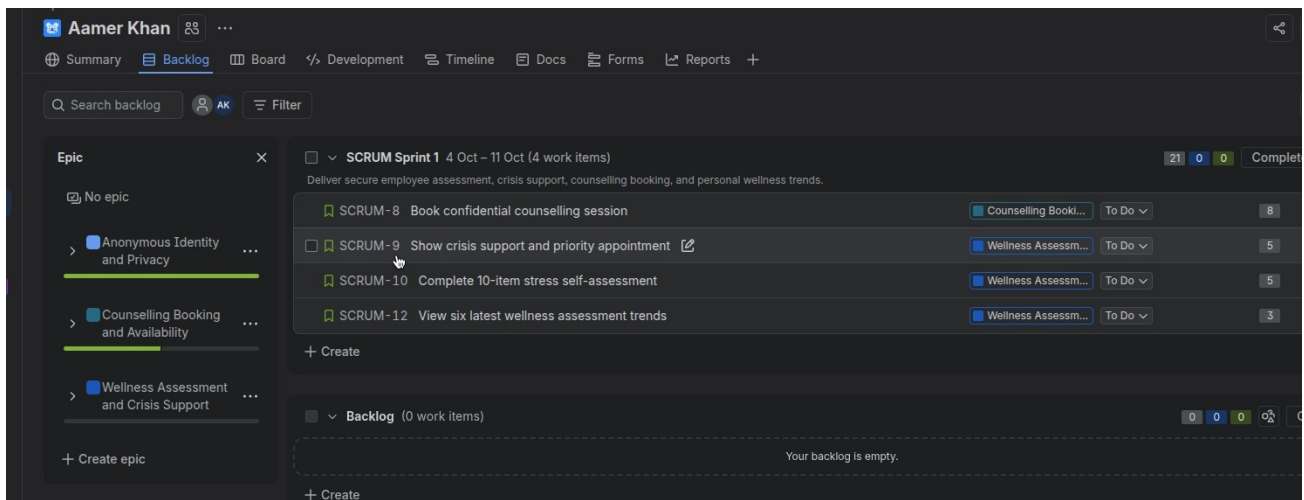


Figure 1: Jira backlog with the Epic panel open; current sprint stories show their parent Epic, status and assigned story points.

2. Story Point Assignments and Sprint Planning

Story points were assigned using Fibonacci values to represent relative effort, complexity and uncertainty. The six relevant stories total 31 points: one 3-point story, four 5-point stories and one 8-point story. The 8-point confidential-booking story is the largest because it combines availability validation, transactional slot locking, timezone handling, pseudo-ID use and confirmation.

Key / Story	Summary	Priority	Points
SCRUM-2	Publish therapist availability	High	5
SCRUM-7	Generate anonymous pseudo-ID	High	5
SCRUM-8	Book confidential counselling session	High	8
SCRUM-9	Show crisis support and priority appointment	High	5
SCRUM-10	Complete 10-item stress self-assessment	High	5
SCRUM-12	View six latest wellness assessment trends	Medium	3

The corrected one-week SCRUM Sprint 1 runs from 4 October to 11 October 2026 with a sprint goal to deliver secure employee assessment, crisis support, counselling booking and personal wellness trends. It contains four stories worth 21 points. The remaining 10 points belong to previously completed pseudo-ID and therapist-availability stories.

3. Sprint Board Simulation

The sprint was simulated by moving work through the Scrum workflow. Figure 2 captures an intermediate state with two stories in To Do, one in Progress and one Done, directly demonstrating movement across the board before the remaining work was completed.

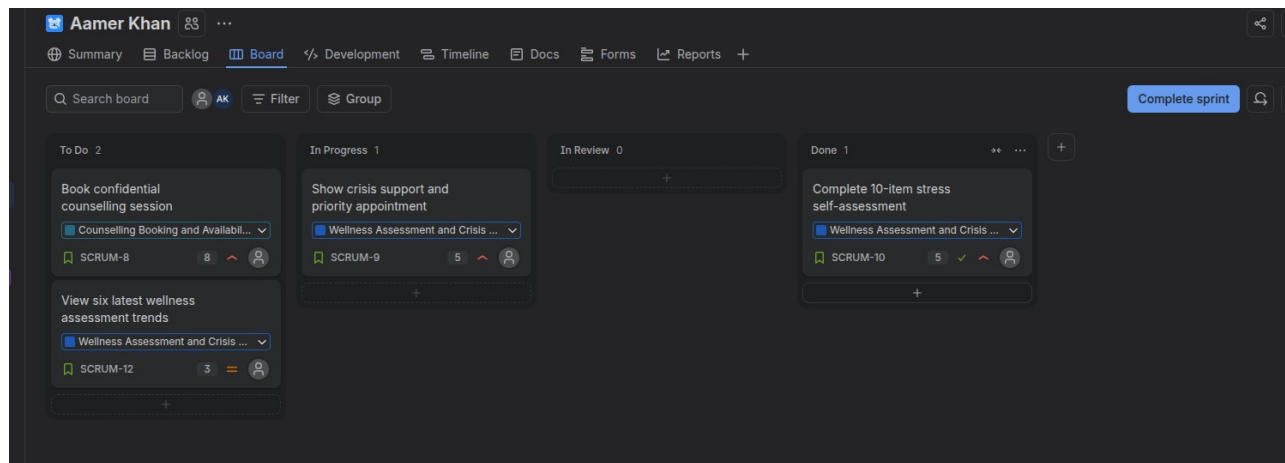


Figure 2: Active Sprint board showing User Stories distributed across To Do, In Progress and Done during the simulation.

4. Burndown and Sprint Outcome

The Sprint Burndown Chart uses story points as the estimation field. The sprint began with 21 points. At the intermediate snapshot, the remaining-work line had fallen to 16 after the 5-point stress self-assessment story was completed, while the grey line shows the ideal burn rate across the one-week sprint.

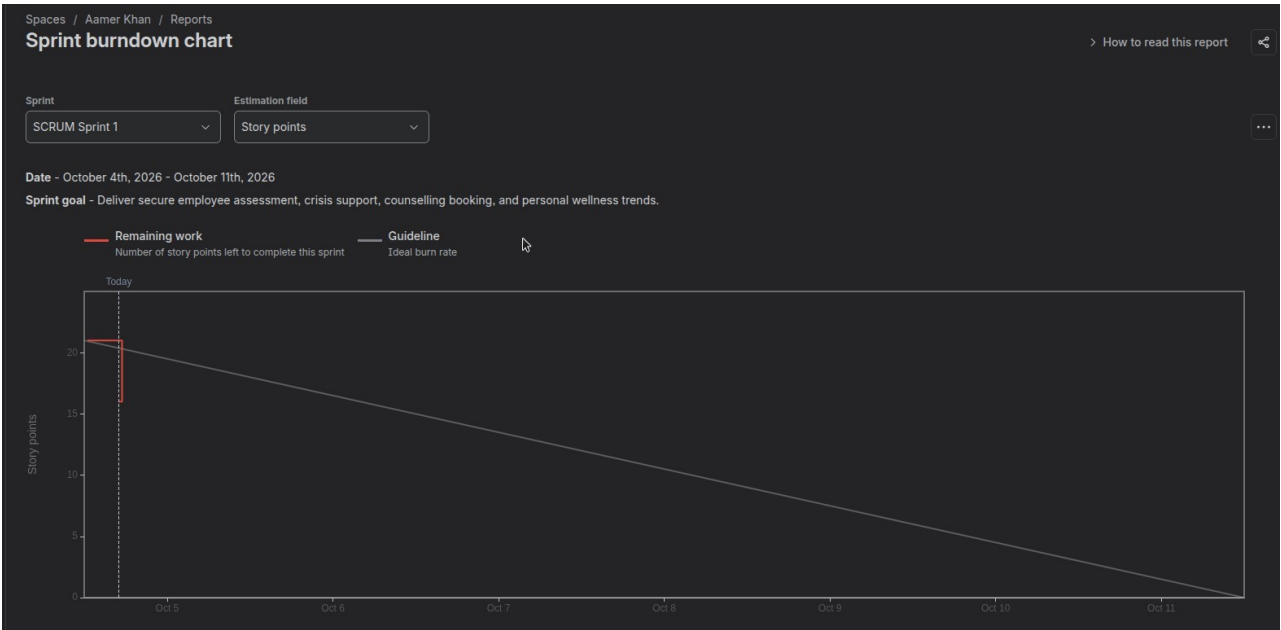


Figure 3: Sprint burndown chart for SCRUM Sprint 1 showing remaining story points against the ideal guideline.

The burnup report provides the complementary view: total sprint scope remained fixed at 21 points while completed work increased until all committed points were delivered. Because this laboratory exercise was simulated in a short period, the completion line rises much faster than it would in a real week-long development sprint.

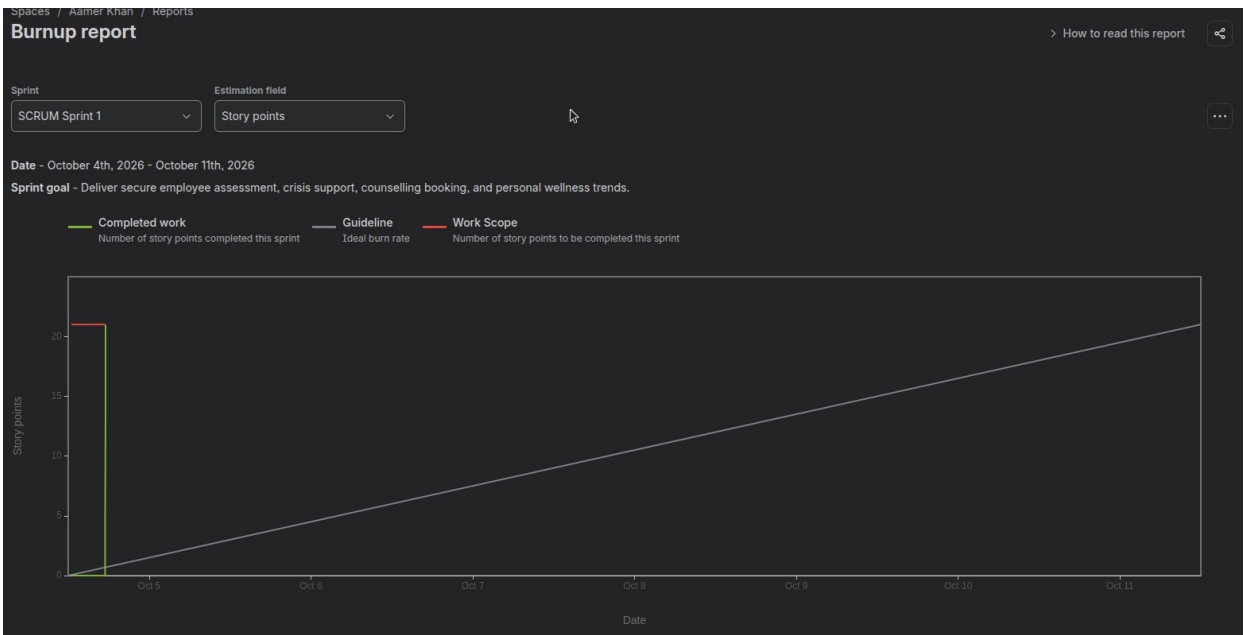


Figure 4: Burnup report showing completed work against the fixed 21-point sprint scope.

4.1 Sprint Completion History

The Jira event history confirms the progression from 0 to 21 completed story points. SCRUM-10 raised completed work from 0 to 5 points, SCRUM-8 from 5 to 13, SCRUM-12 from 13 to 16, and SCRUM-9 from 16 to 21. The sprint was then completed with all four current sprint stories delivered.

Date	Event	Work item	Completed	Scope
Sun, Oct 04 2026, 11:59am	Sprint started	SCRUM-8 Book confidential counselling session SCRUM-9 Show crisis support and priority appointment SCRUM-10 Complete 10-item stress self-assessment SCRUM-12 View six latest wellness assessment trends	0	21
Sun, Oct 04 2026, 4:57pm	Work item completed	SCRUM-10 Complete 10-item stress self-assessment	0 → 5	21
Sun, Oct 04 2026, 5:01pm	Work item completed	SCRUM-8 Book confidential counselling session	5 → 13	21
Sun, Oct 04 2026, 5:01pm	Work item completed	SCRUM-12 View six latest wellness assessment trends	13 → 16	21
Sun, Oct 04 2026, 5:01pm	Work item completed	SCRUM-9 Show crisis support and priority appointment	16 → 21	21
Sun, Oct 04 2026, 5:01pm	Sprint completed	SCRUM-8 Book confidential counselling session SCRUM-9 Show crisis support and priority appointment SCRUM-10 Complete 10-item stress self-assessment SCRUM-12 View six latest wellness assessment trends	21	21

Figure 5: Sprint completion history showing all four User Stories delivered and 21 of 21 committed story points completed.

5. Reflection

5.1 Did our estimations reflect the actual effort?

The estimates were internally consistent with the relative complexity of the stories. The confidential counselling booking story was assigned 8 points because it combines several concerns - slot validation, locking, timezone handling, anonymous identity and confirmation - while the wellness-trend story was assigned 3 points because it is comparatively smaller. The 5-point assessment and crisis-support stories represent medium-sized pieces of work. Since this was a sprint simulation rather than a real implementation sprint, the exercise validates relative estimation more than actual development hours.

5.2 Was our backlog well-prioritized?

Yes. The High-priority stories cover the core safety and trust requirements: anonymous identity, therapist availability, confidential booking, stress assessment and crisis response. The wellness-trend story is Medium priority because it provides useful longitudinal insight but can follow the essential privacy, safety and access functions. This ordering keeps the minimum viable counselling workflow focused on the highest user impact first.

5.3 How did our simulated sprint align with our plan?

The corrected one-week sprint committed 21 story points across four stories and used the project-specific goal of delivering secure employee assessment, crisis support, counselling booking and wellness trends. The active-board snapshot shows the work moving through To Do, In Progress and Done, and the completion history later confirms that all 21 committed points were finished. This means the simulated sprint met its stated scope and goal. Earlier sprint records remain in Jira, but the figures in this report use the corrected counselling sprint because it provides the cleanest evidence for the final submission.

5.4 What insights did the burndown chart give about our team's capacity?

The burndown chart first shows a reduction from 21 to 16 remaining points when the 5-point assessment story was completed. The subsequent completion history shows the remaining work being finished rapidly on the same day. This demonstrates that Jira correctly tracked story-point completion, but the near-vertical burn is a result of the lab simulation and should not be interpreted as sustainable real-world velocity. A real sprint would need work to be completed over several days before the chart could be used to estimate dependable team capacity.

Takeaways

The backlog structure, priority choices and Fibonacci estimates provided a clear basis for sprint planning. For a real implementation, the 8-point booking story would be the first candidate for further decomposition if it proved difficult, while privacy and crisis-support stories should remain at the top of the backlog. Future capacity decisions should be based on one or more real-time sprints rather than the accelerated timing of this simulation.
